



	Nov-13	Dec-13	Jan-14	Feb-14	Mar-14	Apr-14	May-14	Jun-14	Jul-14	Aug-14	Sep-14	Oct-14	Nov-14	Dec-14	Jan-15	Feb-15	Mar-15	Apr-15	May-15
Total Hours - Period	49950	4157	16141	42329	83771	93144	126526	203638	216706	309095	273014	350423	459563	187022	148620	185239	205957	243434	317558
Total Hours - Cumulative	49950	54107	70248	112577	196348	289492	416019	619657	836363	1145458	1418471	1768895	2228457	2415480	2564100	2749339	2955296	3198731	3516289
Concrete Hours - Period	0	0	2019	0	0	0	0	7353	14980	45978	71790	129965	150640	33648	30292	47094	63916	90444	146572
Concrete Hours - Cumulative	0	0	2019	2019	2019	2019	2019	9371	24351	70329	142119	272084	422724	456373	486665	533759	597675	688119	834691
Concrete Placed - Period	0	0	0	0	0	0	0	56	82	3411	7896	9824	6787	1699	995	2801	3600	4873	14300
Concrete Placed - Cumulative	0	0	0	0	0	0	0	56	137	3548	11444	21268	28055	29754	30749	33551	37151	42024	56324

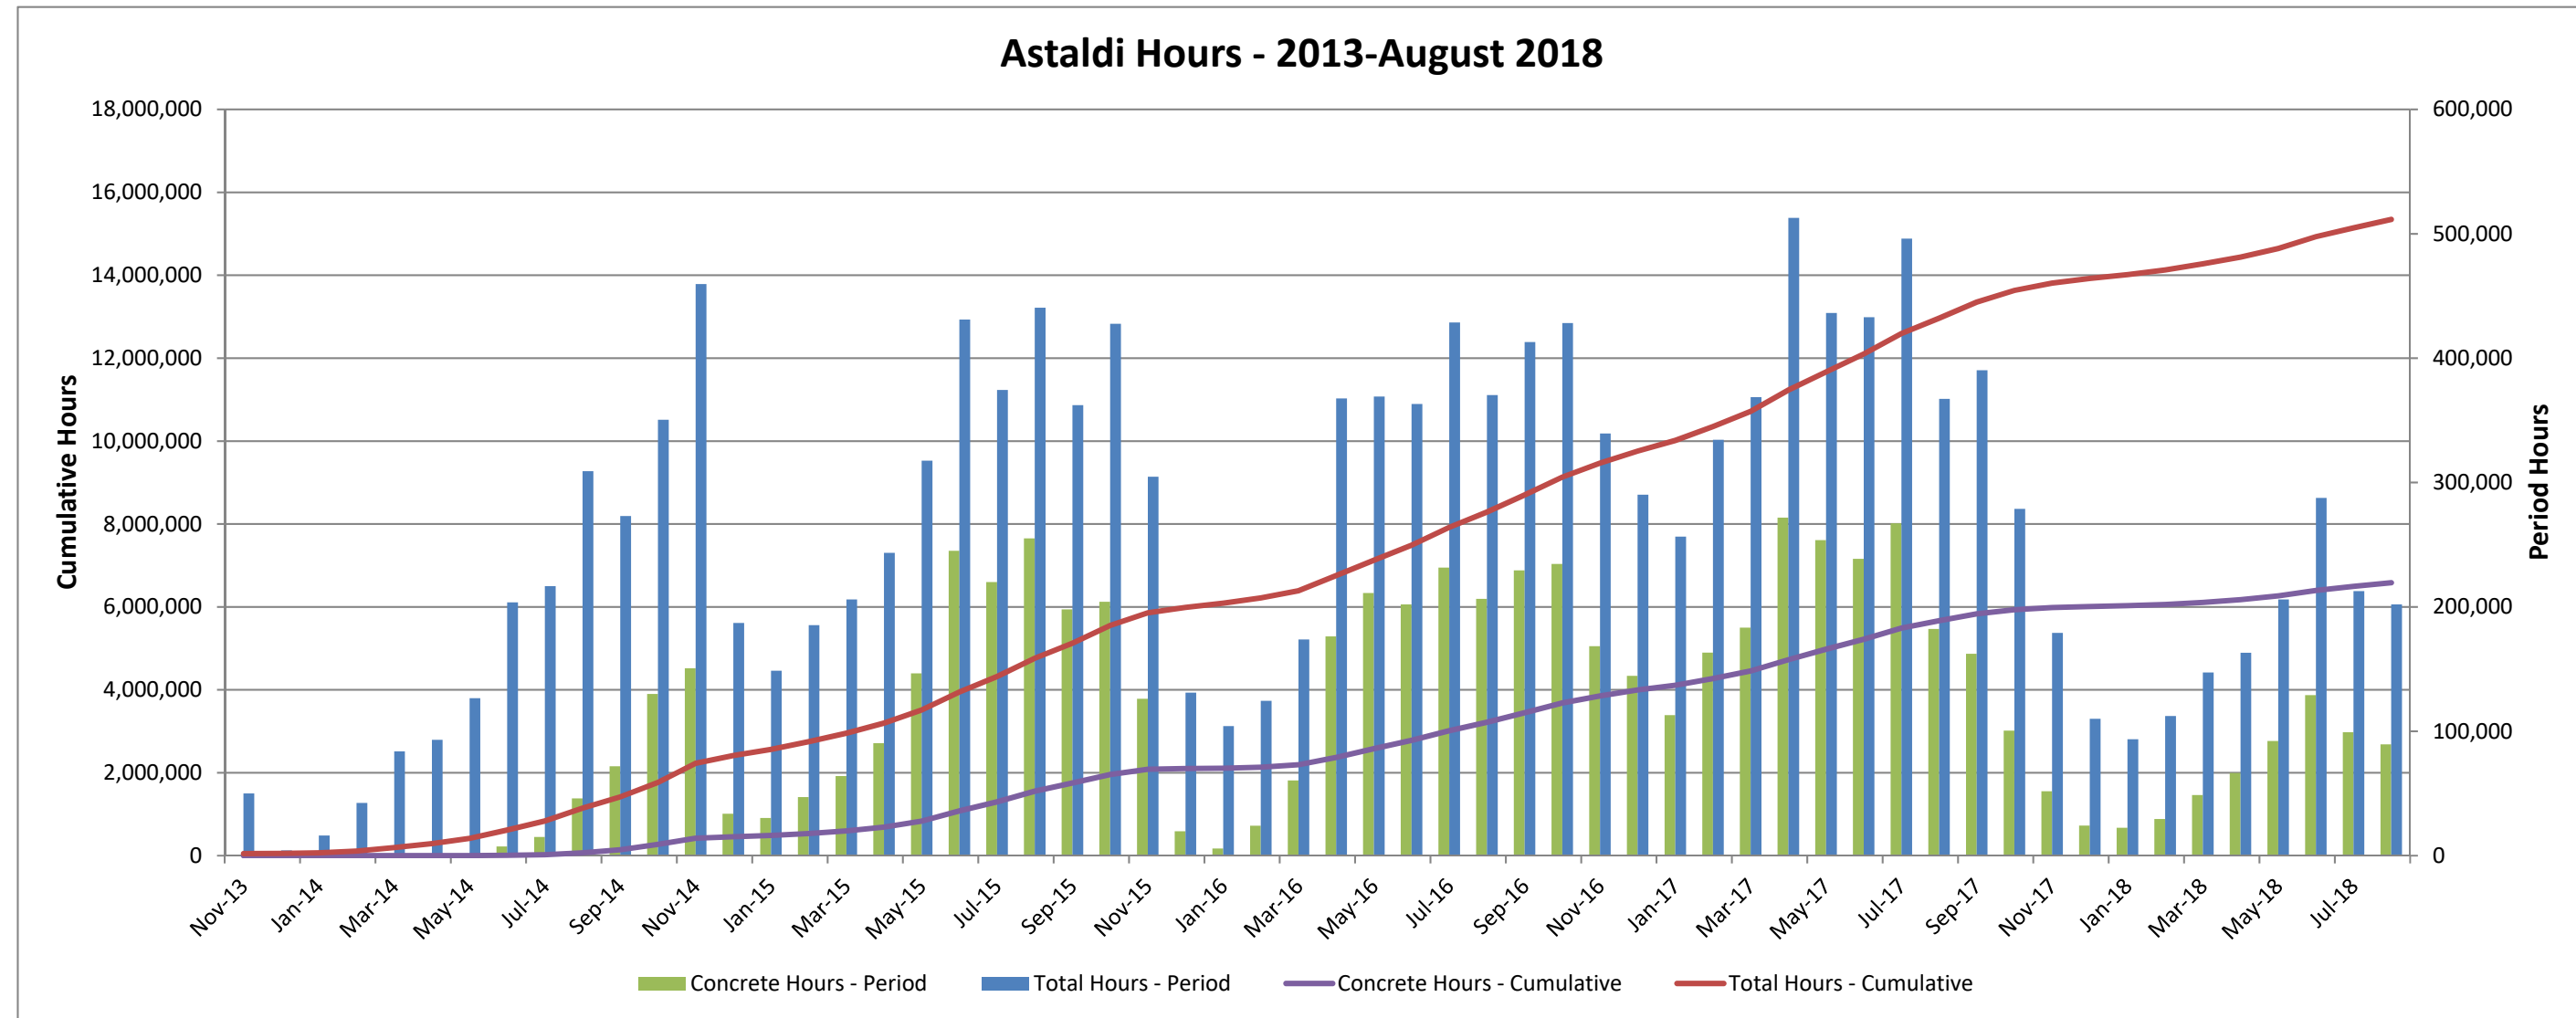

Notes:

1. Hours provided through Astaldi reporting.
2. Total hours includes all indirect and direct hours as reported by Astaldi.
3. Breakout of concrete hours provided by Ataldi; concrete hours includes formwork, rebar and concrete placement. LCP has not validated the breakdown; some concrete hours could be within indirects.
4. November 2013 was the first reporting received from Astaldi and includes all cumulative hours to that point.

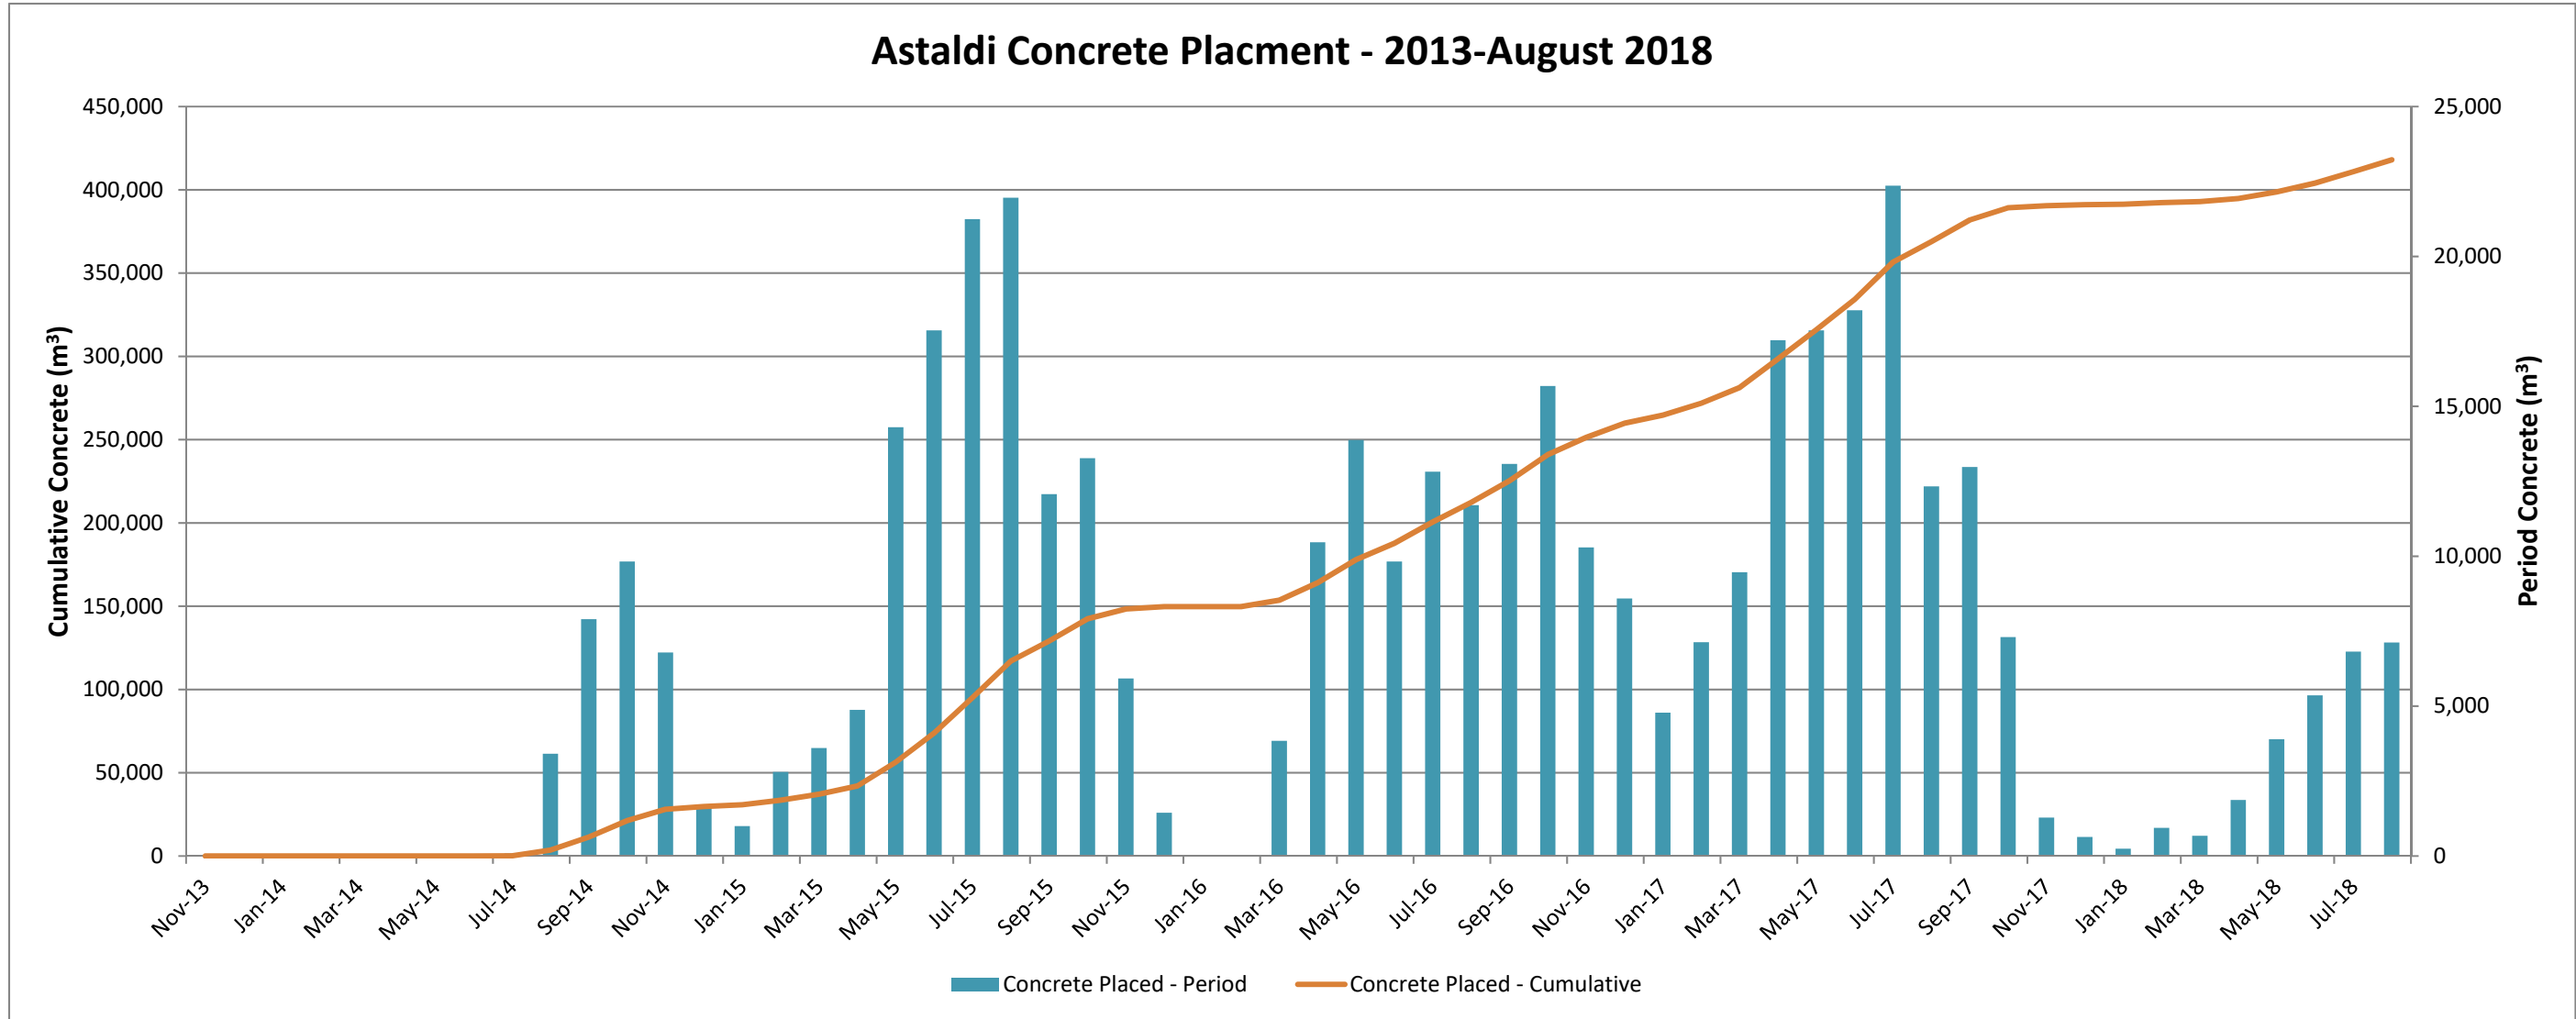

Jun-15	Jul-15	Aug-15	Sep-15	Oct-15	Nov-15	Dec-15	Jan-16	Feb-16	Mar-16	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16	Jan-17	Feb-17
430968	374403	440522	362229	427627	304649	130980	104174	124423	173800	367605	369072	363134	428633	370278	412928	428132	339432	290202	256488	334318
3947257	4321660	4762181	5124411	5552038	5856687	5987666	6091840	6216262	6390062	6757668	7126739	7489873	7918506	8288784	8701712	9129843	9469276	9759477	10015966	10350283
245028	219882	255105	198015	204036	126150	19570	5749	23989	60403	176221	211081	201974	231568	206471	229339	234487	168418	144571	112932	163213
1079718	1299600	1554705	1752720	1956755	2082906	2102476	2108224	2132214	2192617	2368838	2579919	2781893	3013461	3219932	3449271	3683758	3852176	3996747	4109679	4272892
17533	21245	21959	12070	13270	5922	1443	0	0	3839	10464	13875	9823	12817	11701	13079	15678	10294	8590	4782	7131
73858	95102	117061	129131	142401	148323	149766	149766	149766	153605	164069	177945	187767	200585	212286	225366	241043	251338	259928	264710	271841

Mar-17	Apr-17	May-17	Jun-17	Jul-17	Aug-17	Sep-17	Oct-17	Nov-17	Dec-17	Jan-18	Feb-18	Mar-18	Apr-18	May-18	Jun-18	Jul-18	Aug-18
368596	512784	436318	432831	496024	367241	390214	278830	179017	110041	93521	112275	147267	163056	206020	287582	212618	201986
10718879	11231663	11667981	12100811	12596836	12964077	13354291	13633121	13812138	13922179	14015700	14127976	14275243	14438298	14644318	14931900	15144519	15346505
183235	271780	253596	238670	267182	182192	162225	100503	51759	24171	22345	29400	48665	66419	92129	129056	99172	89414
4456127	4727907	4981503	5220173	5487354	5669546	5831771	5932275	5984034	6008204	6030550	6059950	6108615	6175034	6267164	6396220	6495393	6584807
9463	17206	17530	18201	22360	12328	12973	7303	1278	633	240	939	672	1866	3895	5359	6819	7121
281304	298511	316041	334241	356601	368929	381903	389205	390484	391117	391357	392296	392968	394834	398730	404089	410907	418028
